



**WESTSIDE COMMUNITY CENTER  
2932 S IH Frontage Road  
New Braunfels, TX 78130**

**ADA SELF-EVALUATION FACILITY SURVEY**

Conducted by



## **About This Report**

This report has been developed as part of an overall self-evaluation and transition planning effort undertaken by the City of New Braunfels and as required by the Americans with Disabilities Act Title II Regulations for state and local government entities. The conditions cited within this report represent the findings of our team at the time of evaluation on May 11, 2021, and May 12, 2021. Our survey included public areas and other areas where city programs are offered.

## **ADA Standards**

The building or facility was evaluated for compliance with the 2010 ADA Standards. It should be noted that any renovation or alteration projects that are undertaken at this time and in the future must be designed to comply with the 2010 ADA Standards (or the most current adopted standard in effect at the time).

## **Prioritization**

The non-compliant issues cited in this report have been assigned a prioritization for remediation – Priorities 1 through 4. This prioritization system is based upon priorities for barrier removal as published in the ADA Title III (§36.304). Although Title II entities are not required to undertake barrier removal steps in the same way as places of public accommodation, this system is considered a “best practice” for taking the necessary steps to bring buildings and facilities into compliance with the ADA.

Priority 1:	Accessible Approach and Entry
Priority 2:	Access to Goods and Services
Priority 3:	Toilet Rooms
Priority 4:	Additional Access

## **Recommendations and Cost**

For each non-compliant item cited, a recommendation for remediation is included along with a rough order of magnitude cost. It should be noted that in many instances, there may be more than one way to correct an issue. We have made every effort to suggest the most logical and least expensive method of correction; however, other methods may prove to be more easily accomplished or less expensive. Additionally, our recommendations are based upon our visual observations and may not reflect hidden conditions that might render our suggestions infeasible or less cost-effective. The costs provided take in to account materials and labor but do not include any professional design fees.

# New Braunfels Westside Community Center

Prepared by Kim Goss

Jun 29, 2021

## Description

50 tasks in this report.

## Contents

#37 Priority 1: Accessible Routes.....	4
#38 Priority 1: Accessible Routes.....	5
#39 Priority 1: Accessible Routes.....	7
#40 Priority 1: Accessible Routes.....	8
#41 Priority 1: Accessible Routes.....	10
#36 Priority 1: Parking.....	11
#1 Priority 2: Accessible Routes.....	13
#7 Priority 2: Counters.....	14
#4 Priority 2: Doors.....	15
#25 Priority 2: Doors.....	16
#28 Priority 2: Doors.....	18
#27 Priority 2: Elevators.....	20
#35 Priority 2: Reach Range.....	21
#3 Priority 2: Protruding Objects.....	22
#5 Priority 2: Protruding Objects.....	24
#6 Priority 2: Protruding Objects.....	26
#26 Priority 2: Protruding Objects.....	28
#29 Priority 2: Protruding Objects.....	30
#15 Priority 3: Baby Changing Stations.....	32

#12 Priority 3: Toilet Compartments .....	34
#21 Priority 3: Toilet Compartments .....	35
#8 Priority 3: Doors.....	36
#17 Priority 3: Doors.....	37
#30 Priority 3: Doors.....	39
#44 Priority 3: Doors.....	41
#14 Priority 3: Grab Bars.....	43
#22 Priority 3: Grab Bars.....	44
#34 Priority 3: Grab Bars.....	45
#50 Priority 3: Grab Bars.....	46
#16 Priority 3: Showers .....	48
#24 Priority 3: Showers .....	49
#9 Priority 3: Lavatories.....	50
#19 Priority 3: Lavatories.....	52
#32 Priority 3: Lavatories.....	54
#46 Priority 3: Lavatories.....	55
#10 Priority 3: Protruding Objects .....	56
#18 Priority 3: Protruding Objects .....	58
#11 Priority 3: Reach Range .....	60
#20 Priority 3: Reach Range .....	61
#31 Priority 3: Reach Range .....	62
#45 Priority 3: Reach Range .....	63
#13 Priority 3: Water Closets.....	64
#23 Priority 3: Water Closets.....	65
#33 Priority 3: Water Closets.....	66
#42 Priority 3: Water Closets.....	68

#43 Priority 3: Water Closets.....	69
#47 Priority 3: Water Closets.....	71
#48 Priority 3: Water Closets.....	72
#51 Priority 3: Water Closets.....	73
#2 Priority 4: Vending Machines.....	74

## #37 Priority 1: Accessible Routes

### Status

Open

### Location

Route from Public ROW

### Description

Sidewalk has a cross slope of approximately 2.6%.

Recommendation: Remove and replace sidewalk.

(1 panel, 30 SF)

Note: Due to the relatively low severity of the issue, this correction may be considered low priority.

### Sheet

C2




### Cost Impact

300

### Photos



Kim Goss  
May 12, 2021 8:57 AM

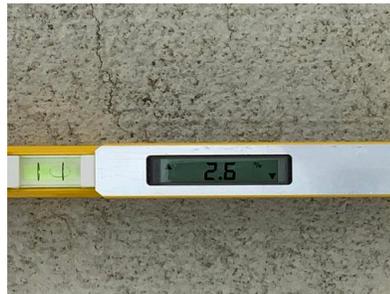

Kim Goss  
May 12, 2021 8:58 AM



Kim Goss  
May 12, 2021 8:58 AM

## #38 Priority 1: Accessible Routes

### Status

Open

### Location

Route from Accessible  
Parking

### Description

A portion of the sidewalk has a cross slope of up to 2.7%, excessive gaps and excessive change in level.

Recommendation: Remove and replace sidewalk. (2 panels, 50 SF)

### Sheet

C2



### Cost Impact

500

### Photos

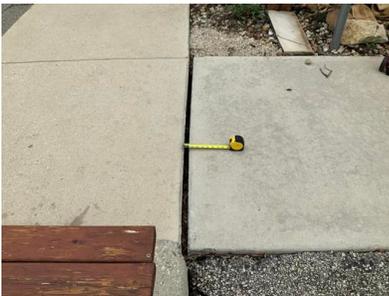


Photo May 12, 9 04 59 AM

Kim Goss

May 12, 2021 9:05 AM



Photo May 12, 9 05 05 AM

Kim Goss

May 12, 2021 9:05 AM



Photo May 12, 9 05 54 AM

Kim Goss

May 12, 2021 9:05 AM



Kim Goss  
May 12, 2021 9:06 AM



Photo May 12, 9 07 24 AM  
Kim Goss  
May 12, 2021 9:07 AM



Photo May 12, 9 07 30 AM  
Kim Goss  
May 12, 2021 9:07 AM



Photo May 12, 9 07 45 AM  
Kim Goss  
May 12, 2021 9:07 AM



Photo May 12, 9 07 51 AM  
Kim Goss  
May 12, 2021 9:07 AM




Figure 303.3 Beveled Change in Level

303.3(a)  
Kim Goss  
Jun 29, 2021 4:13 PM




Figure 302.3 Elongated Openings in Floor or Ground Surfaces

302.3  
Kim Goss  
Jun 29, 2021 4:13 PM

## #39 Priority 1: Accessible Routes

**Status**  
Open

**Sheet**  
C2

**Location**  
Route from Public ROW

**Description**  
The route has an approximate 1" gap on each side of the metal coverplate.

**Recommendation:** Add caulking material.

**Cost Impact**  
200



### Photos



Photo May 12, 8 59 48 AM  
**Kim Goss**  
May 12, 2021 8:59 AM



Photo May 12, 8 59 55 AM  
**Kim Goss**  
May 12, 2021 8:59 AM



Photo May 12, 9 00 06 AM  
**Kim Goss**  
May 12, 2021 9:00 AM




Figure 302.3 Elongated Openings in Floor or Ground Surfaces

392,3

**Kim Goss**

Jun 28, 2021 11:10 AM

## #40 Priority 1: Accessible Routes

**Status**  
Open

**Location**  
Route from Public ROW

**Description**  
Sidewalk has approximate 1" wide openings between panels in two locations.

**Recommendation:** Add caulking material.

**Sheet**  
C2



**Cost Impact**  
200

### Photos



Photo May 12, 9 00 59 AM  
**Kim Goss**  
May 12, 2021 9:00 AM

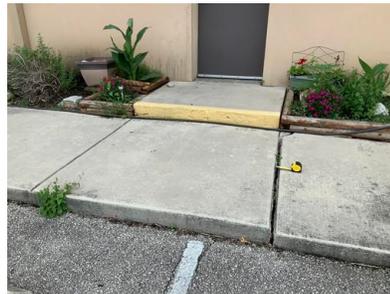


Photo May 12, 9 01 05 AM  
**Kim Goss**  
May 12, 2021 9:01 AM



Photo May 12, 9 01 10 AM  
**Kim Goss**  
May 12, 2021 9:01 AM

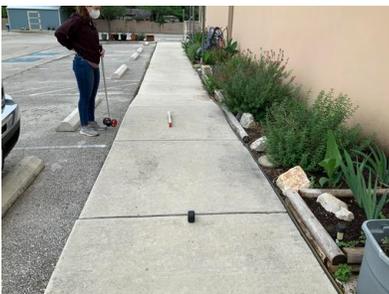


Photo May 12, 9 02 16 AM  
**Kim Goss**  
May 12, 2021 9:02 AM



Photo May 12, 9 02 21 AM  
**Kim Goss**  
May 12, 2021 9:02 AM



Photo May 12, 9 02 27 AM  
**Kim Goss**  
May 12, 2021 9:02 AM




Figure 302.3 Elongated Openings in Floor or Ground Surfaces

302.3

**Kim Goss**

Jun 29, 2021 4:17 PM

## #41 Priority 1: Accessible Routes

**Status**  
Open

**Location**  
Route from Accessible Parking

**Description**  
Sidewalk has approximate 1" wide openings between panels in two locations.

**Recommendation:** Add caulking material.

**Sheet**  
C2



**Cost Impact**  
200

### Photos



Photo May 12, 9 09 10 AM  
**Kim Goss**  
 May 12, 2021 9:09 AM



Photo May 12, 9 09 15 AM  
**Kim Goss**  
 May 12, 2021 9:09 AM



Photo May 12, 9 09 29 AM  
**Kim Goss**  
 May 12, 2021 9:09 AM

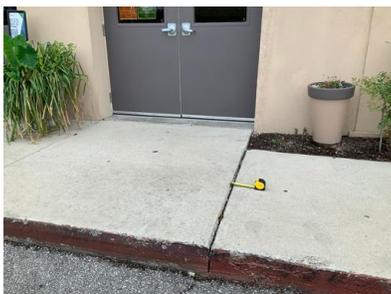


Photo May 12, 9 09 35 AM  
**Kim Goss**  
 May 12, 2021 9:09 AM



Photo May 12, 9 09 41 AM  
**Kim Goss**  
 May 12, 2021 9:09 AM




Figure 302.3 Elongated Openings in Floor or Ground Surfaces

302.3  
**Kim Goss**  
 Jun 29, 2021 4:19 PM

## #36 Priority 1: Parking

### Status

Open

### Location

Parking Lot

### Description

All 4 accessible parking spaces and access aisles have running slopes ranging from 4.3% to 5.9% and a crack in the asphalt.

Recommendation: Remove and replace asphalt in this area.

### Sheet

C2



### Cost Impact

13500

### Photos



Photo May 12, 8 51 51 AM

**Kim Goss**

May 12, 2021 8:51 AM



Photo May 12, 8 51 59 AM

**Kim Goss**

May 12, 2021 8:51 AM



Photo May 12, 8 52 17 AM

**Kim Goss**

May 12, 2021 8:52 AM



Photo May 12, 8 52 26 AM

**Kim Goss**

May 12, 2021 8:52 AM



Photo May 12, 8 52 40 AM

**Kim Goss**

May 12, 2021 8:52 AM



Photo May 12, 8 52 52 AM

**Kim Goss**

May 12, 2021 8:52 AM



Photo May 12, 8 53 06 AM

**Kim Goss**

May 12, 2021 8:53 AM



Photo May 12, 8 53 15 AM

**Kim Goss**

May 12, 2021 8:53 AM



Photo May 12, 8 54 05 AM

**Kim Goss**

May 12, 2021 8:54 AM



Photo May 12, 8 54 11 AM

**Kim Goss**

May 12, 2021 8:54 AM



**Kim Goss**

May 12, 2021 8:56 AM

## #1 Priority 2: Accessible Routes

### Status

Open

### Location

Stage

### Description

No accessible route is provided to the stage or vending machines.

Recommendation: Install a platform lift for access to the stage.

### Photos



Kim Goss  
May 11, 2021 3:02 PM




Kim Goss  
May 11, 2021 3:02 PM



Kim Goss  
May 11, 2021 3:02 PM

### Sheet

A1

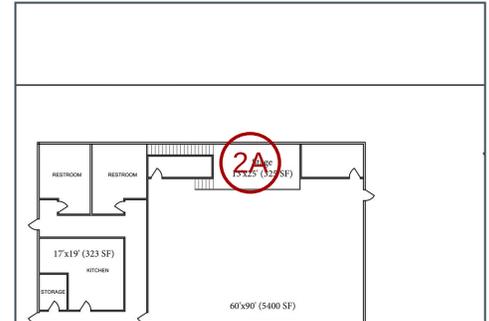

### Cost Impact

10000

## #7 Priority 2: Counters


**Status**  
Open

**Location**  
Lunchroom Corridor

**Description**  
The kitchen serving counter is 35" high.

Recommendation: Modify at least a portion of counter to a maximum 34" height.

**Sheet**  
A1

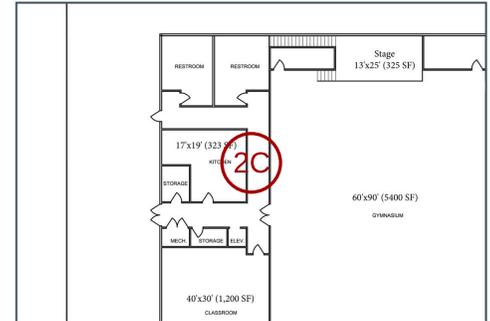

**Cost Impact**  
3500

### Photos



Kim Goss  
May 11, 2021 3:12 PM



Kim Goss  
May 11, 2021 3:12 PM



Kim Goss  
May 11, 2021 3:12 PM




Figure 308.3.2 Obstructed High Side Reach

308.3.2

Kim Goss  
Jun 28, 2021 11:22 AM

## #4 Priority 2: Doors


**Status**  
Open

**Location**  
Lunchroom/Classroom

**Description**  
Door has only 16" of clearance past the latch on the pull side.


**Recommendation:** Modify door configuration to provide a minimum 18" clearance past the latch.

**Sheet**  
A1

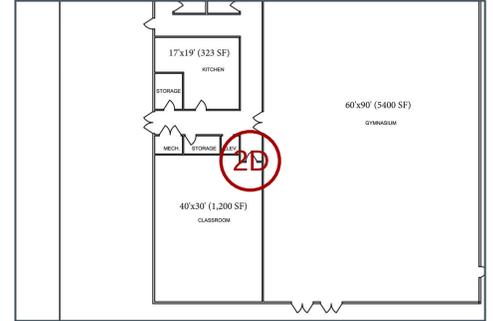

**Cost Impact**  
2750

### Photos



404.2.4.1(a)  
**Kim Goss**  
May 16, 2020 12:37 PM



**Kim Goss**  
May 11, 2021 3:08 PM



**Kim Goss**  
May 11, 2021 3:08 PM



**Kim Goss**  
May 11, 2021 3:08 PM

## #25 Priority 2: Doors


**Status**  
Open

**Location**  
Gymnasium

**Description**  
Two sets of double doors have vision panels positioned with the bottom of the glass 44" high.

**Recommendation:** Replace doors with ones have vision panels positioned with the bottom no more than 43".  
(Note: If the doors were installed prior to March 15, 2012, they may enjoy safe harbor until replaced.)

**Sheet**  
A1

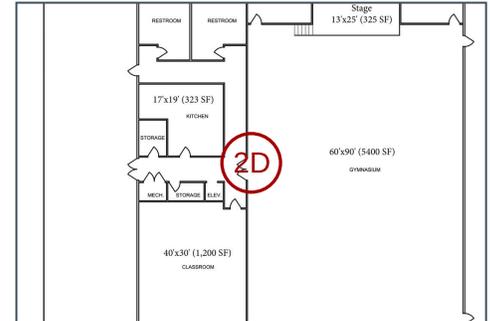

**Cost Impact**  
3000

### Photos



Kim Goss  
May 11, 2021 3:40 PM



Kim Goss  
May 11, 2021 3:40 PM



Kim Goss  
May 11, 2021 3:40 PM



**Kim Goss**

May 11, 2021 3:41 PM

---

## #28 Priority 2: Doors

### Status

Open

### Location

Upstairs Corridor


### Description

Vision panels in 4 doors have the bottom of the glass positioned 45-1/2" high.

Recommendation: Replace doors with ones have vision panels positioned with the bottom no more than 43".  
(Note: If the doors were installed prior to March 15, 2012, they may enjoy safe harbor until replaced.)

### Sheet

A1

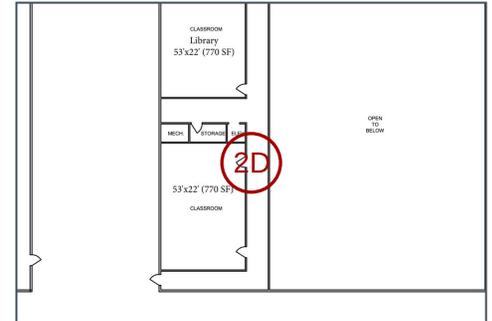

### Cost Impact

3000

### Photos

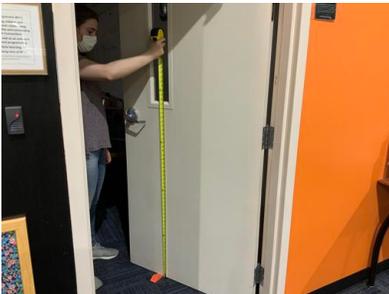


Photo May 11, 3 45 02 PM  
**Kim Goss**  
May 11, 2021 3:45 PM



Photo May 11, 3 45 08 PM  
**Kim Goss**  
May 11, 2021 3:45 PM



**Kim Goss**  
May 11, 2021 3:46 PM



**Kim Goss**  
May 11, 2021 3:46 PM



**Kim Goss**  
May 11, 2021 3:46 PM



**Kim Goss**  
May 11, 2021 3:46 PM

## #27 Priority 2: Elevators

**Status**  
Open

**Location**  
Elevator

**Description**  
The emergency alarm button is centered 31" high.

Recommendation: Relocate panel with alarm button 35" high minimum.

### Photos




**Kim Goss**  
May 11, 2021 3:44 PM



**Kim Goss**  
May 11, 2021 3:44 PM

**Sheet**  
A1

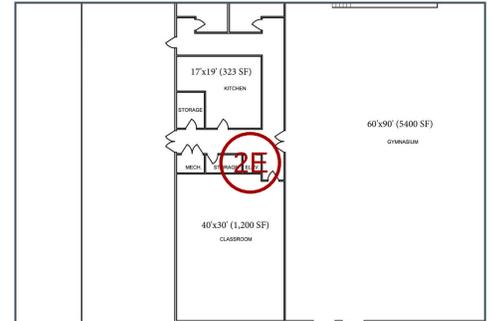

**Cost Impact**  
1000

## #35 Priority 2: Reach Range

**Status**  
Open

**Location**  
Library

**Description**  
Coat hooks are positioned  
66" high.

Recommendation: Install at  
least one hook no higher  
than 48".

### Photos

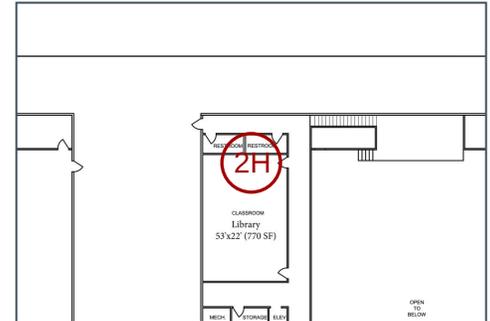


Photo May 11, 4 01 03 PM  
**Kim Goss**  
May 11, 2021 4:01 PM



Photo May 11, 4 01 10 PM  
**Kim Goss**  
May 11, 2021 4:01 PM

**Sheet**  
A1



**Cost Impact**  
50

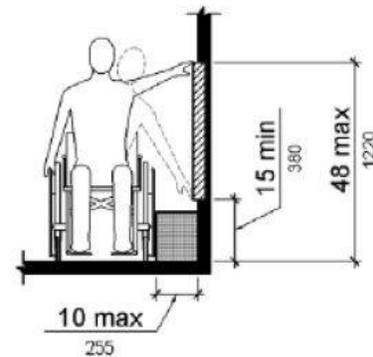


Figure 308.3.1 Unobstructed Side Reach

308.3.1  
**Kim Goss**  
Jun 29, 2021 4:26 PM

### #3 Priority 2: Protruding Objects


**Status**  
Open

**Location**  
Lunchroom Corridor

**Description**  
The bleeding control kit projects 10" at 45" high.

**Recommendation:** Relocate or add cane barrier below.

**Sheet**  
A1

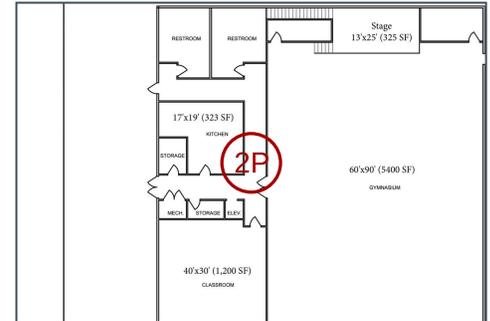

**Cost Impact**  
500

### Photos



Photo May 11, 3 05 56 PM  
**Kim Goss**  
May 11, 2021 3:05 PM



Photo May 11, 3 06 03 PM  
**Kim Goss**  
May 11, 2021 3:06 PM



Photo May 11, 3 06 11 PM  
**Kim Goss**  
May 11, 2021 3:06 PM

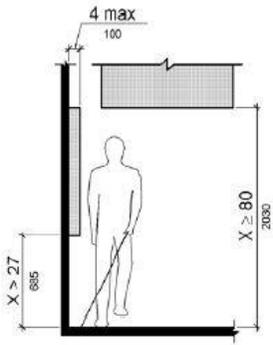


Figure 307.2 Limits of Protruding Objects

307.2

Kim Goss

Jun 29, 2021 4:28 PM

## #5 Priority 2: Protruding Objects

### Status

Open

### Location

Elevator Lobby


### Description

Drinking fountains project approximately 7" from the base at 28-1/2" and 32" high.

Recommendation: Lower accessible fountain so the bottom of the apron is exactly 27", and install an apron to the high fountain.

### Sheet

A1

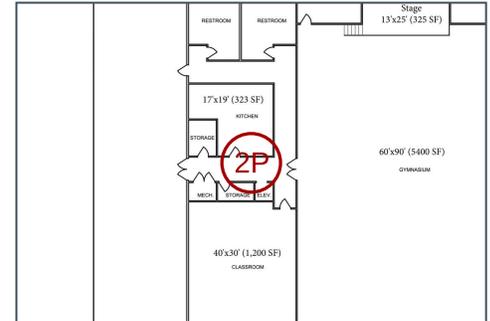

### Cost Impact

3700

### Photos



Photo May 11, 3 08 00 PM

Kim Goss

May 11, 2021 3:08 PM



Photo May 11, 3 08 55 PM

Kim Goss

May 11, 2021 3:08 PM



Photo May 11, 3 09 02 PM

Kim Goss

May 11, 2021 3:09 PM



Photo May 11, 3 09 17 PM  
**Kim Goss**  
May 11, 2021 3:09 PM




Photo May 11, 3 09 25 PM  
**Kim Goss**  
May 11, 2021 3:09 PM



Photo May 11, 3 09 30 PM  
**Kim Goss**  
May 11, 2021 3:09 PM



Photo May 11, 3 09 36 PM  
**Kim Goss**  
May 11, 2021 3:09 PM

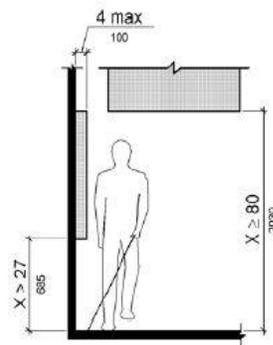

**Figure 307.2 Limits of Protruding Objects**

307.2  
**Kim Goss**  
Jun 29, 2021 4:32 PM

## #6 Priority 2: Protruding Objects

### Status

Open

### Location

Elevator Lobby


### Description

The defibrillator box projects 7-1/2" at 48" high.

Recommendation: Relocate box or install a partially recessed model.

### Sheet

A1

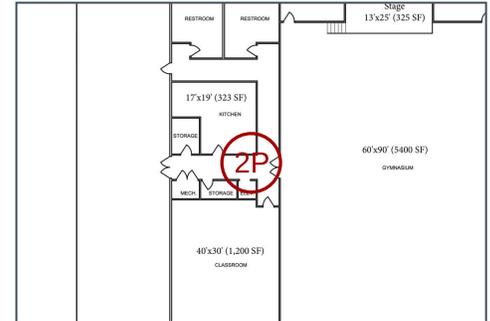

### Cost Impact

500


### Photos



Kim Goss  
May 11, 2021 3:11 PM



Kim Goss  
May 11, 2021 3:11 PM

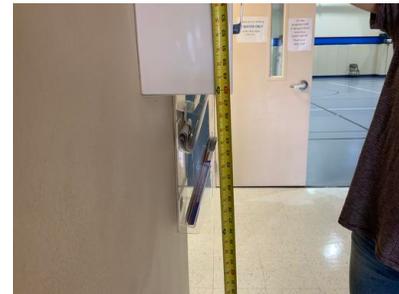

Kim Goss  
May 11, 2021 3:11 PM



Kim Goss

May 11, 2021 3:11 PM

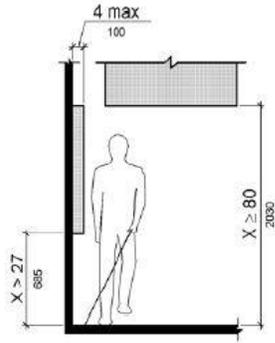


Figure 307.2 Limits of Protruding Objects

307.2

Kim Goss

Jun 28, 2021 11:20 AM

## #26 Priority 2: Protruding Objects


**Status**  
Open

**Location**  
Elevator Lobby

**Description**  
Alarm panel box projects 5" from the wall at 52" high.

**Recommendation:** Provide cane barrier below.

**Sheet**  
A1

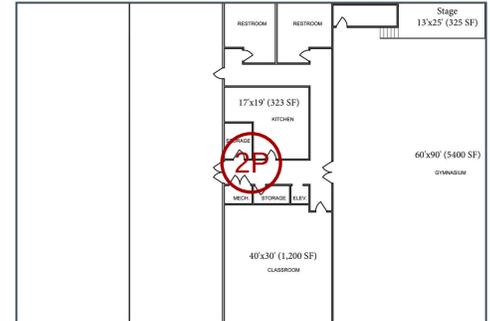

**Cost Impact**  
500

### Photos



Kim Goss  
May 11, 2021 3:42 PM



Kim Goss  
May 11, 2021 3:42 PM



Kim Goss  
May 11, 2021 3:42 PM

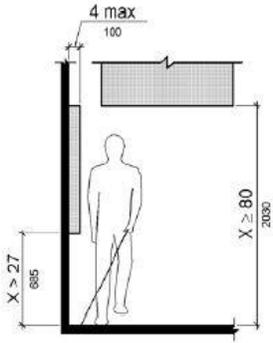


Figure 307.2 Limits of Protruding Objects

307.2

Kim Goss

Jun 28, 2021 11:17 AM

## #29 Priority 2: Protruding Objects

### Status

Open

### Location

Upstairs Corridor


### Description

The high drinking fountain projects approximately 7" from the base at 33" high.

Recommendation: Install an apron to the high fountain to bring the bottom to no more than 27" high.

### Sheet

A1

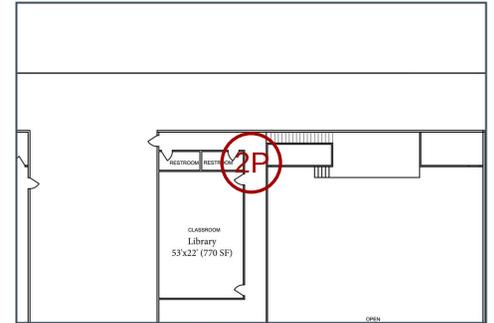

### Cost Impact

300

### Photos



Kim Goss  
May 11, 2021 3:48 PM



Kim Goss  
May 11, 2021 3:48 PM



Kim Goss  
May 11, 2021 3:48 PM

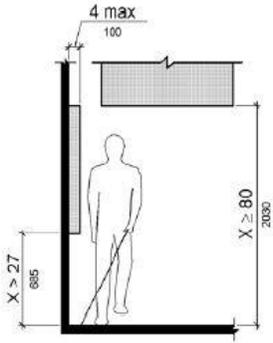


Figure 307.2 Limits of Protruding Objects

307.2

Kim Goss

Jun 28, 2021 1:39 PM

## #15 Priority 3: Baby Changing Stations

### Status

Open

### Location

Women's Restroom


### Description

The baby changing station requires a side reach height of 51" to open and has a surface slope of approximately 7.5% within the clear floor space.

Recommendation: Replace baby changing station and locate it where the floor is level and outside of circulation paths. TDLR requires baby changing stations to be considered in their open position when considering protruding objects.

### Sheet

A1

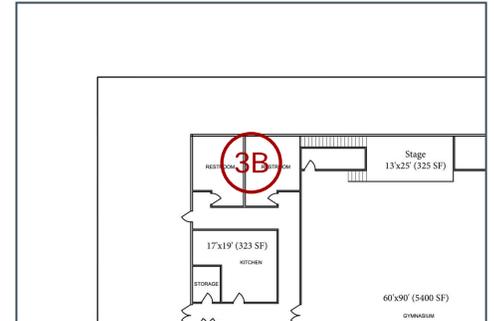

### Cost Impact

1000

### Photos



Photo May 11, 3 24 26 PM  
**Kim Goss**  
May 11, 2021 3:24 PM



Photo May 11, 3 24 29 PM  
**Kim Goss**  
May 11, 2021 3:24 PM



Photo May 11, 3 24 47 PM  
**Kim Goss**  
May 11, 2021 3:24 PM



Photo May 11, 3 24 51 PM

**Kim Goss**

May 11, 2021 3:24 PM



Photo May 11, 3 26 13 PM

**Kim Goss**

May 11, 2021 3:26 PM



Photo May 11, 3 26 19 PM

**Kim Goss**

May 11, 2021 3:26 PM

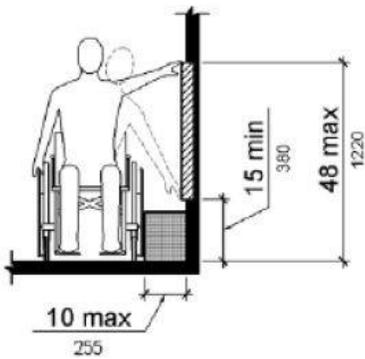


Figure 308.3.1 Unobstructed Side Reach

308.3.1

**Kim Goss**

Jun 29, 2021 4:35 PM

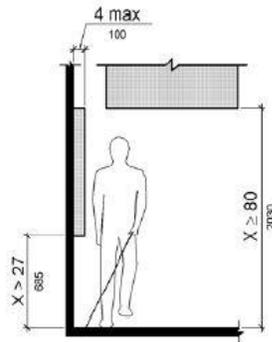


Figure 307.2 Limits of Protruding Objects

307.2

**Kim Goss**

Jun 29, 2021 4:35 PM

## #12 Priority 3: Toilet Compartments

### Status

Open

### Location

Women's Restroom


### Description

The door to the wheelchair accessible toilet stall is not self-closing and does not have a pull on the inside.

Recommendation: Adjust door hinges. Install door pull.

### Sheet

A1

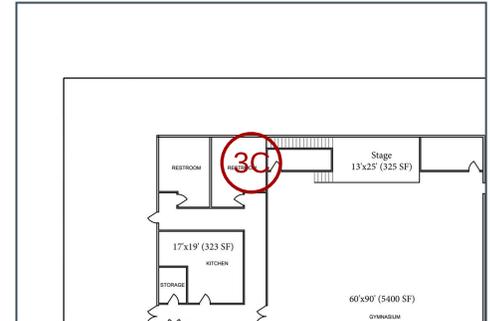


### Cost Impact

325

### Photos



Kim Goss  
May 11, 2021 3:22 PM

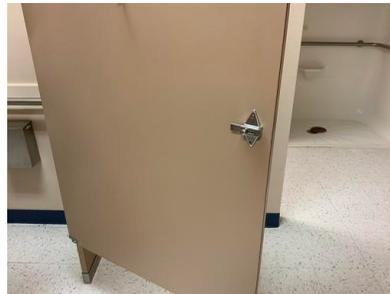

Kim Goss  
May 11, 2021 3:22 PM

## #21 Priority 3: Toilet Compartments

### Status

Open

### Location

Men's Restroom


### Description

The door to the wheelchair accessible toilet stall is not self-closing and does not have a pull on the inside.

Recommendation: Adjust door hinges. Install door pull.

### Sheet

A1

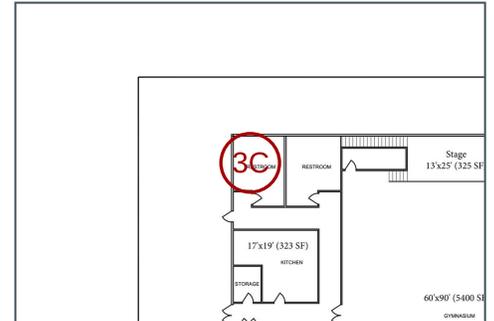

### Cost Impact

325

### Photos



Kim Goss  
May 11, 2021 3:36 PM



Kim Goss  
May 11, 2021 3:36 PM

## #8 Priority 3: Doors

### Status

Open

### Location


Women's Restroom

### Description

Restroom entry door has only 51" of side approach clearance.

Recommendation: Modify toilet partitions to provide a full 54".

### Photos



404.2.4.1(i)

Kim Goss

May 16, 2020 12:29 PM



Kim Goss

May 11, 2021 3:16 PM




Kim Goss

May 11, 2021 3:16 PM

### Sheet

A1

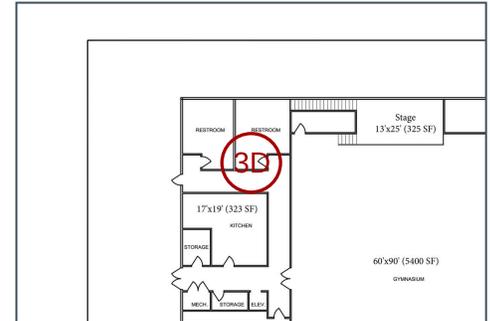

### Cost Impact

1250

## #17 Priority 3: Doors

**Status**  
Open


**Location**  
Men's Restroom

**Description**  
Restroom entry door has only 53" of side approach clearance.

Recommendation: Modify toilet partition to provide a full 54".


Note: Due to the relatively low severity of the issue, this correction may be considered low priority.

**Sheet**  
A1

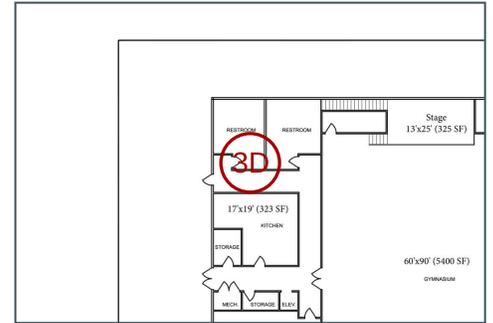

**Cost Impact**  
1250

### Photos



404.2.4.1(i)  
Kim Goss  
May 16, 2020 12:29 PM



Kim Goss  
May 11, 2021 3:33 PM



Kim Goss  
May 11, 2021 3:33 PM



**Kim Goss**

May 11, 2021 3:33 PM

---

### #30 Priority 3: Doors


**Status**  
Open

**Location**  
Upstairs Women's Restroom

**Description**  
The door has a side approach width of only 40-1/2".


Recommendation: Install automatic door opener.  
Alternatively, replace lavatory with a more shallow fixture, swing door outward and remove closer.

**Sheet**  
A1

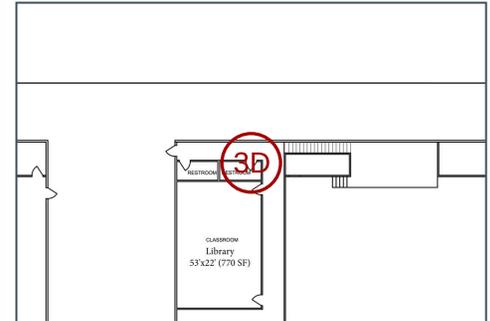


**Cost Impact**  
4000

### Photos

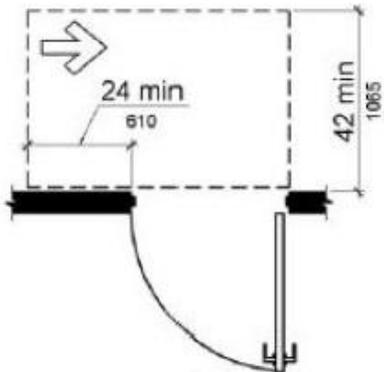

404.2.4.1(j)  
Kim Goss  
May 16, 2020 12:29 PM



404.2.4.1(i)  
Kim Goss  
May 16, 2020 12:29 PM



Photo May 11, 3 50 30 PM  
Kim Goss  
May 11, 2021 3:50 PM



**Kim Goss**

May 11, 2021 3:50 PM

---

## #44 Priority 3: Doors


**Status**  
Open

**Location**  
Upstairs Men's Restroom


**Description**  
The door has a side approach width of only 39-1/2".

Recommendation: Install automatic door opener.  
Alternatively, replace lavatory with a more shallow fixture, swing door outward and remove closer.

### Photos

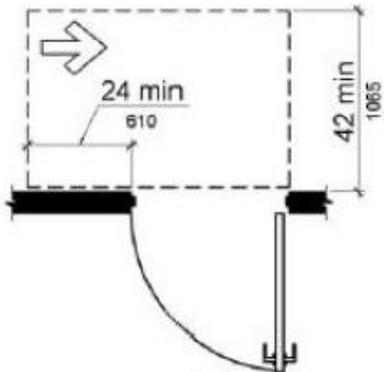


404.2.4.1(j)  
Kim Goss  
May 16, 2020 12:29 PM



404.2.4.1(i)  
Kim Goss  
May 16, 2020 12:29 PM

**Sheet**  
A1

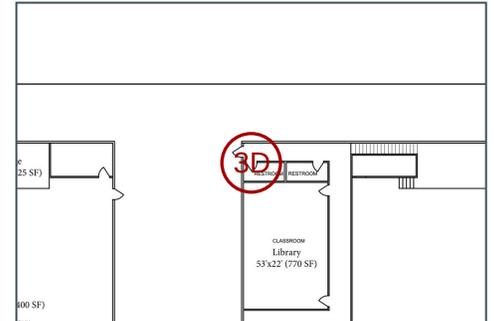

**Cost Impact**  
4000



Photo May 11, 3 56 17 PM  
Kim Goss  
May 11, 2021 3:56 PM



Photo May 11, 3 56 22 PM

**Kim Goss**

May 11, 2021 3:56 PM

---

## #14 Priority 3: Grab Bars

### Status

Open

### Location

Women's Restroom

### Description

The rear grab bar in the wheelchair accessible toilet stall has only 1" of clearance below the bar.


### Recommendation:

Reposition bar to 1-1/2" above toilet tank.

(Note: If this element was installed prior to March 15, 2012, it may enjoy safe harbor until replaced.)

### Sheet

A1

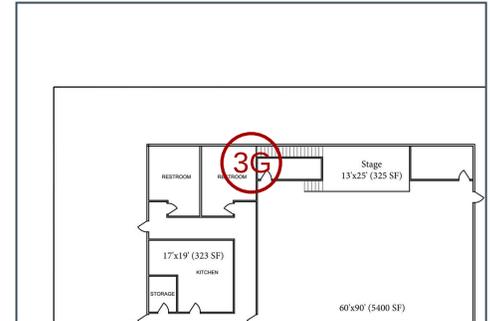

### Cost Impact

200

### Photos



Kim Goss  
May 11, 2021 3:23 PM



Kim Goss  
May 11, 2021 3:23 PM

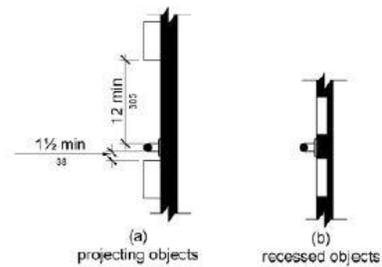


Figure 609.3 Spacing of Grab Bars

609.3

Kim Goss

Jun 28, 2021 1:28 PM

## #22 Priority 3: Grab Bars

### Status

Open

### Location

Men's Restroom

### Description

The rear grab bar in the wheelchair accessible toilet stall has only 1" of clearance below the bar.


### Recommendation:

Reposition bar to 1-1/2" above toilet tank.

(Note: If this element was installed prior to March 15, 2012, it may enjoy safe harbor until replaced.)

### Sheet

A1

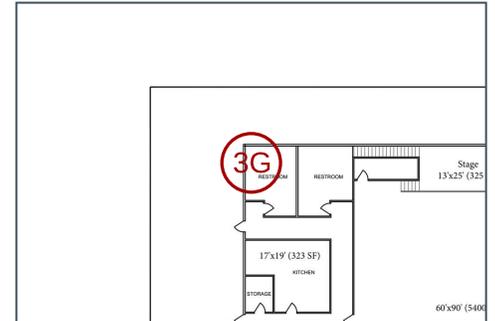

### Cost Impact

200

### Photos



Kim Goss  
May 11, 2021 3:38 PM



Kim Goss  
May 11, 2021 3:38 PM

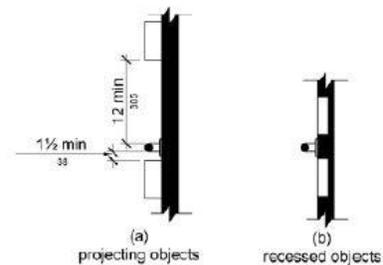


Figure 609.3 Spacing of Grab Bars

609.3

Kim Goss

Jun 28, 2021 1:25 PM

### #34 Priority 3: Grab Bars

**Status**  
Open

**Location**  
Upstairs Women's Restroom

**Description**  
The side grab bar is only 36" long and extends only 48" from the rear wall.

**Recommendation:** Replace with a minimum 42" long grab bar extending 54" from the back wall.

### Photos



Kim Goss  
May 11, 2021 3:54 PM




Kim Goss  
May 11, 2021 3:55 PM



Kim Goss  
May 11, 2021 3:55 PM

**Sheet**  
A1

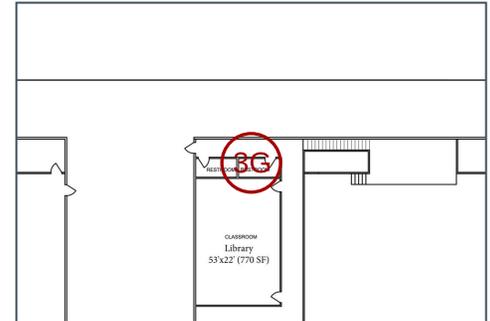

**Cost Impact**  
285




Figure 604.5.1 Side Wall Grab Bar at Water Closets

604.5.1  
Kim Goss  
Jun 28, 2021 2:04 PM

## #50 Priority 3: Grab Bars

### Status

Open

### Location

Upstairs Men's Restroom


### Description

The side grab bar is only 36" long and extends only 48" from the rear wall.

Recommendation: Replace with a minimum 42" long grab bar extending 54" from the back wall.

### Sheet

A1

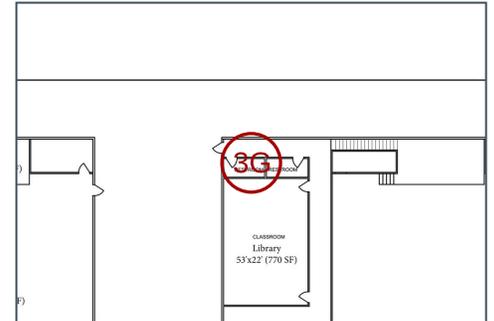

### Cost Impact

285

### Photos



Photo May 11, 3 57 24 PM

Kim Goss

May 11, 2021 3:57 PM



Photo May 11, 3 57 28 PM

Kim Goss

May 11, 2021 3:57 PM



Photo May 11, 3 57 31 PM

Kim Goss

May 11, 2021 3:57 PM




Figure 604.5.1 Side Wall Grab Bar at Water Closets

604.5.1

Kim Goss

Jun 28, 2021 2:20 PM

## #16 Priority 3: Showers

### Status

Open

### Location

Women's Restroom


### Description

The accessible shower is not equipped with a handheld shower wand (missing), and the knob adjustment requires tight grasping and twisting of the wrist.

Recommendation: Install a compliant handheld shower assembly.

### Sheet

A1

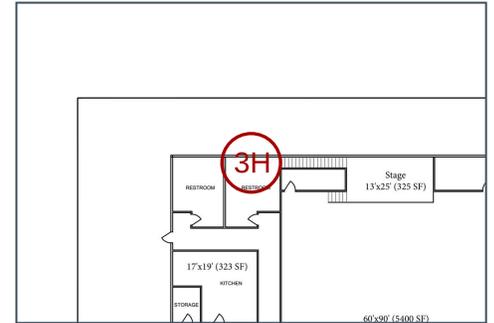

### Cost Impact

600

### Photos



Kim Goss  
May 11, 2021 3:29 PM



Kim Goss  
May 11, 2021 3:29 PM



Kim Goss  
May 11, 2021 3:29 PM

## #24 Priority 3: Showers

### Status

Open

### Location

Men's Restroom

### Description

The accessible shower is not equipped with a handheld shower wand (missing), and the knob adjustment requires tight grasping and twisting of the wrist.

Recommendation: Install a compliant handheld shower assembly.

### Photos




Kim Goss  
May 11, 2021 3:39 PM



Kim Goss  
May 11, 2021 3:39 PM

### Sheet

A1

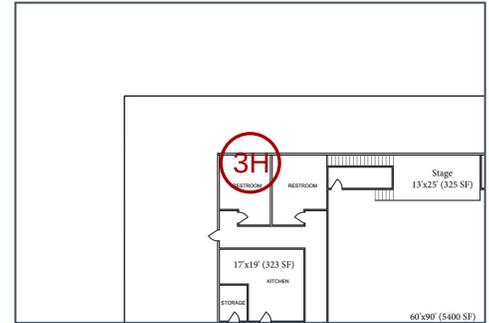

### Cost Impact

600

## #9 Priority 3: Lavatories

### Status

Open

### Location

Women's Restroom

### Description

The lavatory has a rim height of 35" and no knee space below.

### Recommendation:

Reconfigure lavatory with rim 34" high maximum and knee and toe space for a forward approach.

### Photos



Kim Goss  
May 11, 2021 3:18 PM




Kim Goss  
May 11, 2021 3:18 PM



Kim Goss  
May 11, 2021 3:18 PM

### Sheet

A1

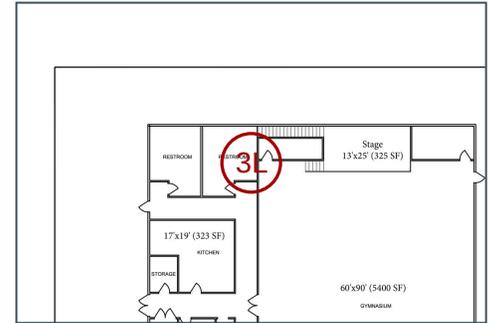

### Cost Impact

1750



Kim Goss

May 11, 2021 3:18 PM




Figure 306.2 Toe Clearance

306.2

Kim Goss

Jun 28, 2021 1:26 PM




Figure 306.3 Knee Clearance

306.3

Kim Goss

Jun 28, 2021 1:26 PM

## #19 Priority 3: Lavatories

### Status

Open

### Location

Men's Restroom

### Description

The lavatory has a rim height of 35" and no knee space below.

### Recommendation:

Reconfigure lavatory with rim 34" high maximum and knee and toe space for a forward approach.

### Photos




Kim Goss  
 May 11, 2021 3:35 PM



Kim Goss  
 May 11, 2021 3:35 PM

### Sheet

A1

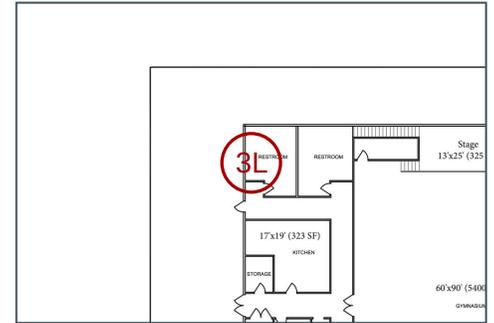

### Cost Impact

1750




Figure 306.3 Knee Clearance

306.3

Kim Goss

Jun 28, 2021 1:21 PM




Figure 306.2 Toe Clearance

306.2

Kim Goss

Jun 28, 2021 1:21 PM

## #32 Priority 3: Lavatories

### Status

Open

### Location

Upstairs Women's Restroom

### Description

Lavatory drainpipes do not have insulation.

Recommendation: Install pipe insulation kit.

### Photos




Kim Goss

May 11, 2021 3:52 PM

### Sheet

A1

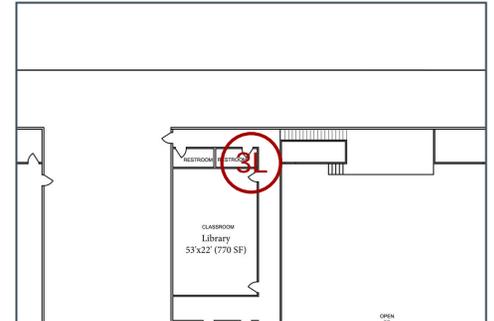

### Cost Impact

200

## #46 Priority 3: Lavatories

### Status

Open

### Location

Upstairs Men's Restroom

### Description

Lavatory drainpipes do not have insulation.

Recommendation: Install pipe insulation kit.

### Photos




Photo May 11, 3 56 38 PM

**Kim Goss**

May 11, 2021 3:56 PM

### Sheet

A1

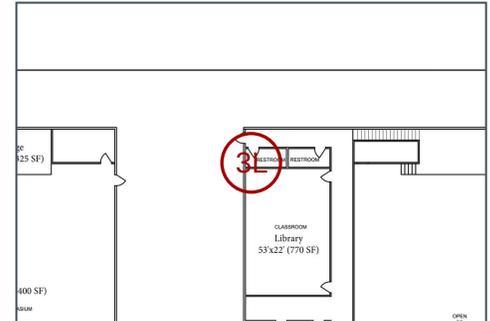

### Cost Impact

200

## #10 Priority 3: Protruding Objects

### Status

Open

### Location

Women's Restroom

### Description

The paper towel dispenser projects 9" at a 47" high.

Recommendation: Relocate dispenser.

### Sheet

A1



### Cost Impact

500

### Photos



Kim Goss  
May 11, 2021 3:23 PM



Kim Goss  
May 11, 2021 3:23 PM



Kim Goss  
May 11, 2021 3:23 PM

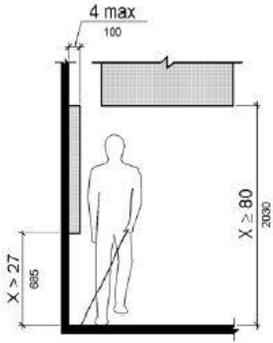


Figure 307.2 Limits of Protruding Objects

307.2

Kim Goss

Jun 28, 2021 12:06 PM

## #18 Priority 3: Protruding Objects


**Status**  
Open

**Location**  
Men's Restroom

**Description**  
The paper towel dispenser projects 9" at a 47" high.

**Recommendation:** Relocate dispenser.

**Sheet**  
A1

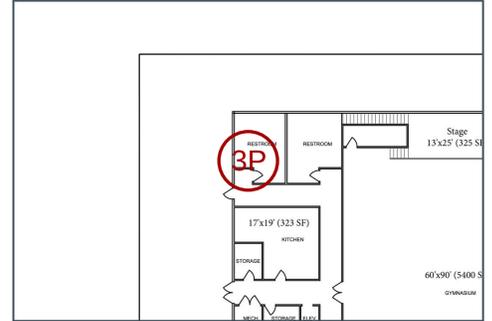

**Cost Impact**  
500

### Photos



Kim Goss  
May 11, 2021 3:34 PM



Kim Goss  
May 11, 2021 3:34 PM



Kim Goss  
May 11, 2021 3:34 PM

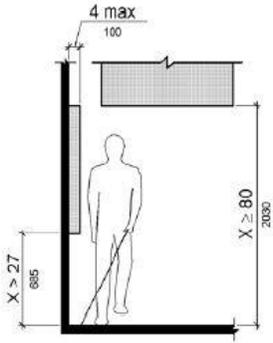


Figure 307.2 Limits of Protruding Objects

307.2

Kim Goss

Jun 28, 2021 12:06 PM

## #11 Priority 3: Reach Range

### Status

Open

### Location

Women's Restroom

### Description

The coat hook in the wheelchair accessible toilet stall is mounted 53" high.

Recommendation: Install hook at a maximum height of 48".

(Note: If this element was installed prior to March 15, 2012, it may enjoy safe harbor until replaced.)

### Photos




Kim Goss  
May 11, 2021 3:21 PM



Kim Goss  
May 11, 2021 3:21 PM

### Sheet

A1

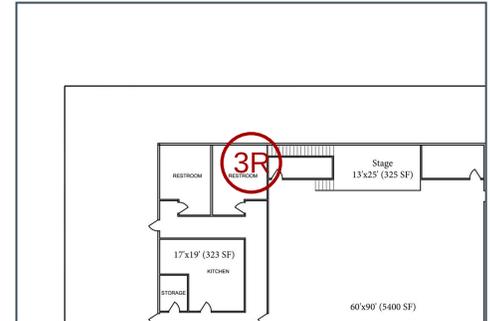

### Cost Impact

50

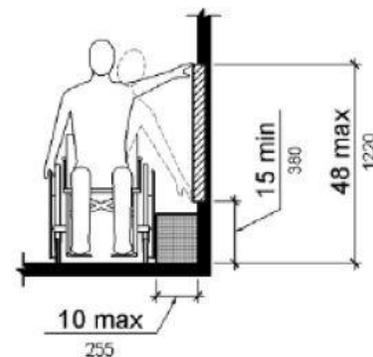


Figure 308.3.1 Unobstructed Side Reach

308.3.1

Kim Goss

Jun 29, 2021 4:39 PM

## #20 Priority 3: Reach Range

### Status

Open

### Location

Men's Restroom

### Description


The coat hook in the wheelchair accessible toilet stall is mounted 53" high.

Recommendation: Install hook at a maximum height of 48".

(Note: If this element was installed prior to March 15, 2012, it may enjoy safe harbor until replaced.)

### Sheet

A1

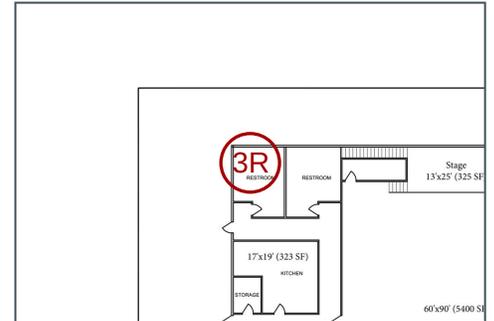

### Cost Impact

50

### Photos



Kim Goss  
May 11, 2021 3:36 PM



Kim Goss  
May 11, 2021 3:36 PM

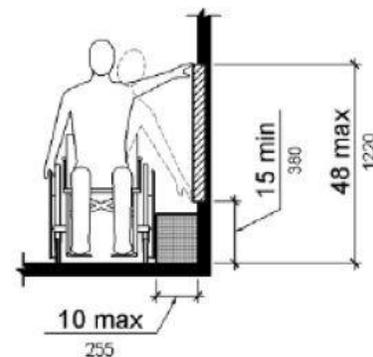


Figure 308.3.1 Unobstructed Side Reach

308.3.1

Kim Goss

Jun 29, 2021 4:39 PM

### #31 Priority 3: Reach Range

**Status**  
Open

**Location**  
Upstairs Women's Restroom


**Description**  
Coat hook is mounted 68" high.

Recommendation: Install a coat hook no higher than 48".

### Photos




Kim Goss  
May 11, 2021 3:51 PM

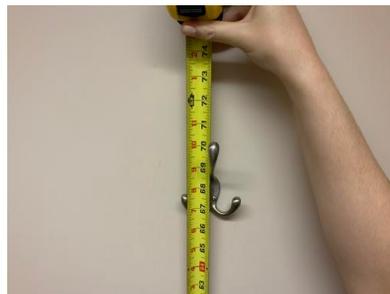

Kim Goss  
May 11, 2021 3:51 PM

**Sheet**  
A1

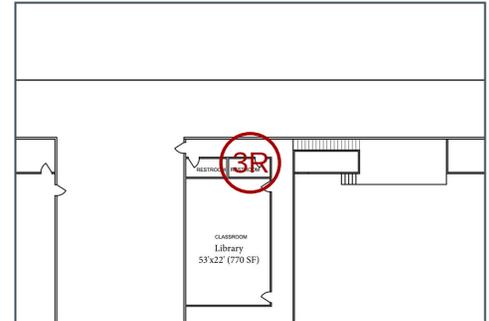

**Cost Impact**  
50

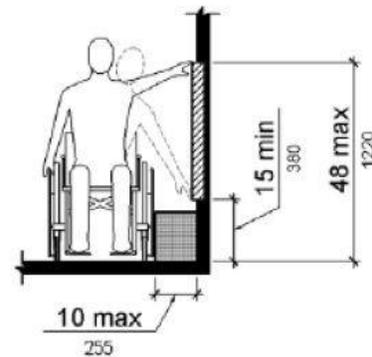


Figure 308.3.1 Unobstructed Side Reach

308.3.1  
Kim Goss  
Jun 28, 2021 1:52 PM

## #45 Priority 3: Reach Range

**Status**  
Open

**Location**  
Upstairs Men's Restroom

**Description**  
Coat hook is mounted 68" high.

Recommendation: Install a coat hook no higher than 48".

### Photos

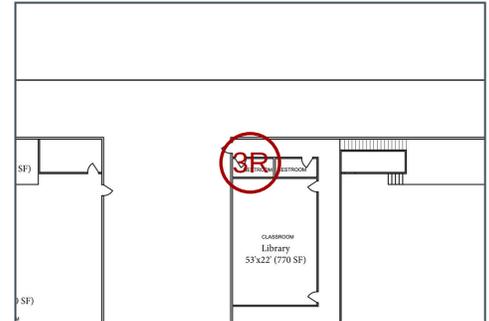


Photo May 11, 3 56 50 PM  
**Kim Goss**  
May 11, 2021 3:56 PM



Photo May 11, 3 56 55 PM  
**Kim Goss**  
May 11, 2021 3:56 PM

**Sheet**  
A1



**Cost Impact**  
50

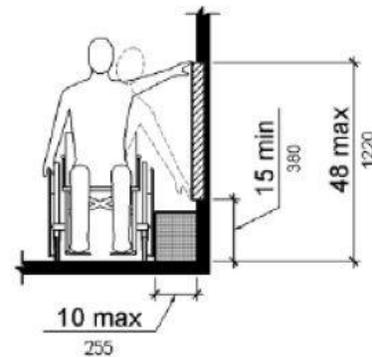


Figure 308.3.1 Unobstructed Side Reach

308.3.1  
**Kim Goss**  
Jun 28, 2021 2:07 PM

## #13 Priority 3: Water Closets

### Status

Open

### Location

Women's Restroom

### Description


The toilet paper dispenser in the wheelchair accessible toilet stall is centered 4" from the front of the water closet.

### Recommendation:

Reposition dispenser with centerline 7" to 9" in front of water closet.

(Note: If this element was installed prior to March 15, 2012, it may enjoy safe harbor until replaced.)

### Photos

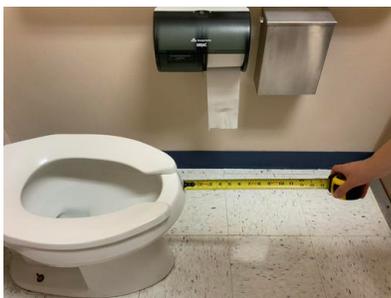

Kim Goss  
May 11, 2021 3:22 PM


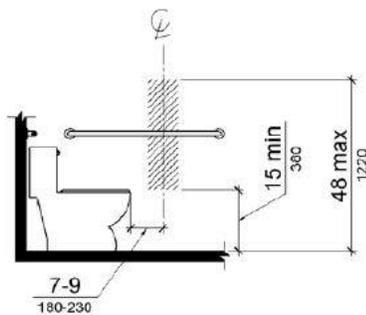


Figure 604.7 Dispenser Outlet Location

604.7  
Kim Goss  
Jun 28, 2021 1:27 PM

### Sheet

A1

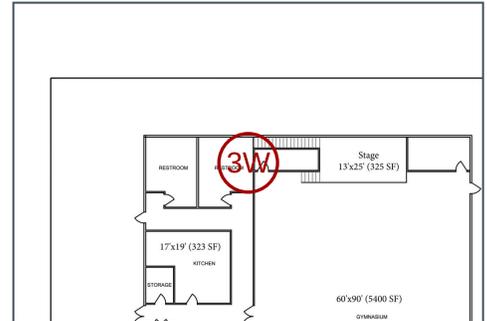

### Cost Impact

225

## #23 Priority 3: Water Closets

### Status

Open

### Location

Men's Restroom

### Description

The toilet paper dispenser in the wheelchair accessible toilet stall is centered 4" from the front of the water closet.


### Recommendation:

Reposition dispenser with centerline 7" to 9" in front of water closet.

(Note: If this element was installed prior to March 15, 2012, it may enjoy safe harbor until replaced.)

### Sheet

A1

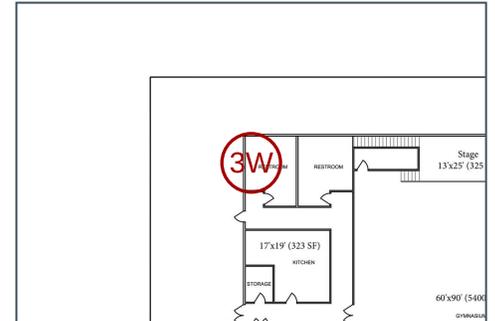

### Cost Impact

225

### Photos



Kim Goss  
May 11, 2021 3:38 PM

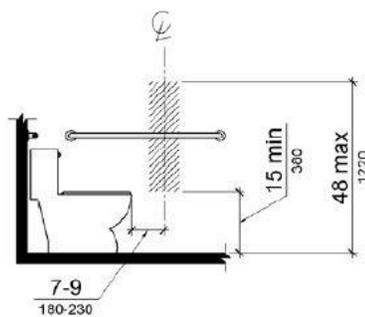


Figure 604.7 Dispenser Outlet Location

604.7  
Kim Goss  
Jun 28, 2021 1:20 PM

### #33 Priority 3: Water Closets

**Status**

Open

**Location**

Upstairs Women's Restroom

**Description**

Water closet is centered 18-1/2" from side wall and seat height is only 16".


Recommendation: Replace water closet and install with centerline 16" to 18" from wall. Ensure seat height of 17" to 19".

(Note: If this element was installed prior to March 15, 2012, the centerline dimension may enjoy safe harbor until replaced. Add a thicker seat to achieve a height of 17" to 19".)

**Photos**


**Sheet**

A1

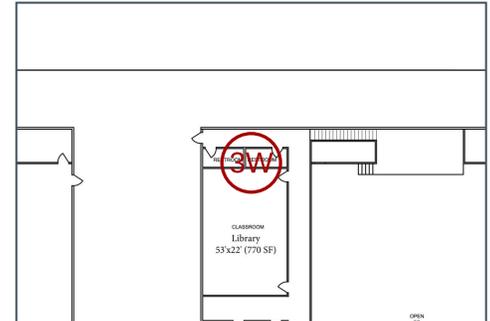

**Cost Impact**

2625



(a)  
wheelchair  
accessible  
water closets

604.2 (a)

Kim Goss

May 16, 2020 1:40 PM



Photo May 11, 3 53 09 PM

Kim Goss

May 11, 2021 3:53 PM



Photo May 11, 3 53 17 PM

Kim Goss

May 11, 2021 3:53 PM



Kim Goss

May 11, 2021 3:53 PM



Photo May 11, 3 53 37 PM

Kim Goss

May 11, 2021 3:53 PM

## #42 Priority 3: Water Closets

### Status

Open

### Location

Upstairs Women's Restroom

### Description

The toilet paper dispenser is centered 4" from the front of the water closet.


### Recommendation:

Reposition dispenser with centerline 7" to 9" in front of water closet.

(Note: If this element was installed prior to March 15, 2012, it may enjoy safe harbor until replaced.)

### Sheet

A1

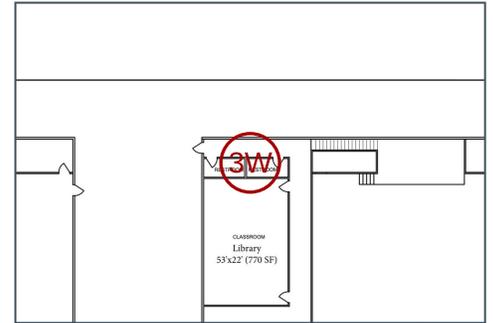

### Cost Impact

225

### Photos



Photo May 11, 3 55 17 PM

Kim Goss

May 11, 2021 3:55 PM

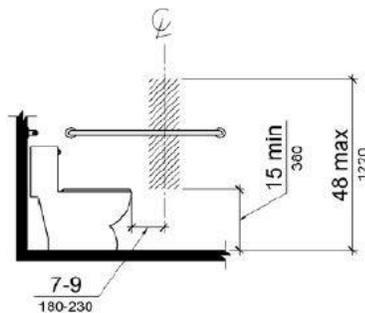


Figure 604.7 Dispenser Outlet Location

604.7

Kim Goss

Jun 28, 2021 2:02 PM

### #43 Priority 3: Water Closets


**Status**  
Open

**Location**  
Upstairs Women's Restroom

**Description**  
The paper towel dispenser overlaps the 60" wide clear floor space at the water closet.

**Recommendation:** Relocate paper towel dispenser outside of required water closet clearance.  
(Note: If this element was installed prior to March 15, 2012, it may enjoy safe harbor until replaced.)

**Sheet**  
A1

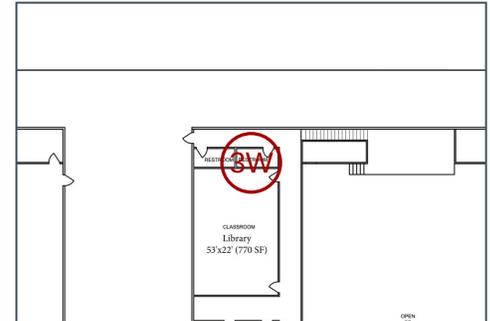

**Cost Impact**  
200

### Photos



Photo May 11, 3 48 56 PM  
**Kim Goss**  
May 11, 2021 3:48 PM



Photo May 11, 3 58 47 PM  
**Kim Goss**  
May 11, 2021 3:58 PM



Photo May 11, 3 58 52 PM  
**Kim Goss**  
May 11, 2021 3:58 PM




Figure 604.3.1 Size of Clearance at Water Closets

604.3.1

Kim Goss

Jun 28, 2021 2:00 PM

## #47 Priority 3: Water Closets

### Status

Open

### Location

Upstairs Men's Restroom


### Description

Water closet has a seat height of only 16", and the flush is mounted on the wall side of the fixture.

Recommendation: Replace water closet.

### Sheet

A1

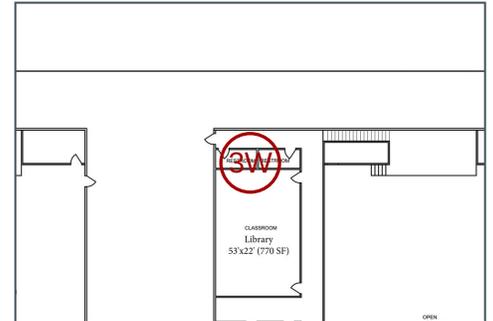

### Cost Impact

1000

### Photos



Photo May 11, 3 55 49 PM

Kim Goss

May 11, 2021 3:55 PM



Photo May 11, 3 57 10 PM

Kim Goss

May 11, 2021 3:57 PM



Photo May 11, 3 57 14 PM

Kim Goss

May 11, 2021 3:57 PM

## #48 Priority 3: Water Closets

### Status

Open

### Location

Upstairs Men's Restroom

### Description


The paper towel dispenser overlaps the 60" wide clear floor space at the water closet.

Recommendation: Relocate paper towel dispenser outside of required water closet clearance.

(Note: If this element was installed prior to March 15, 2012, it may enjoy safe harbor until replaced.)

### Sheet

A1

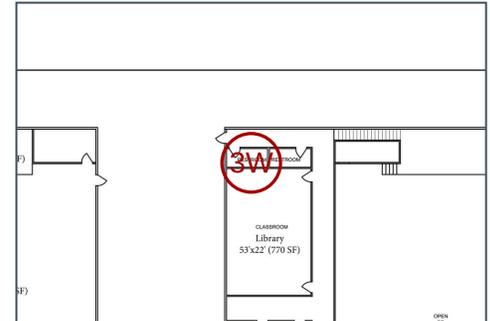

### Cost Impact

200

### Photos



Photo May 11, 3 58 13 PM

Kim Goss

May 11, 2021 3:58 PM



Photo May 11, 3 58 16 PM

Kim Goss

May 11, 2021 3:58 PM




Figure 604.3.1 Size of Clearance at Water Closets

604.3.1

Kim Goss

Jun 28, 2021 2:18 PM

## #51 Priority 3: Water Closets

### Status

Open

### Location

Upstairs Men's Restroom

### Description

The toilet paper dispenser is centered approximately 5" from the front of the water closet.

### Recommendation:

Reposition dispenser with centerline 7" to 9" in front of water closet.

(Note: If this element was installed prior to March 15, 2012, it may enjoy safe harbor until replaced.)

### Photos



Photo May 11, 3 57 24 PM

Kim Goss

May 11, 2021 3:57 PM

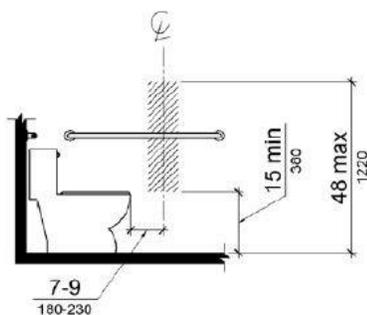


Figure 604.7 Dispenser Outlet Location


604.7

Kim Goss

Jun 28, 2021 2:22 PM

### Sheet

A1

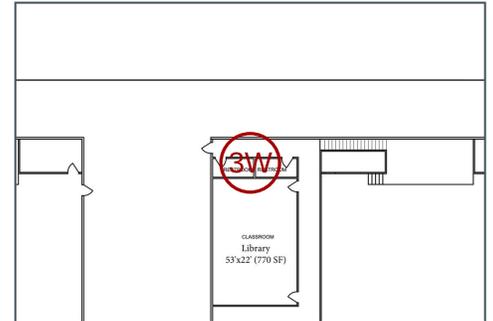

### Cost Impact

225

## #2 Priority 4: Vending Machines

### Status

Open

### Location

Stage

### Description

The card slide at the vending machine is 54" high.

Recommendation: Replace vending machine.

### Photos



Kim Goss  
 May 11, 2021 3:04 PM



Kim Goss  
 May 11, 2021 3:04 PM



Kim Goss  
 May 11, 2021 3:04 PM

### Sheet

A1

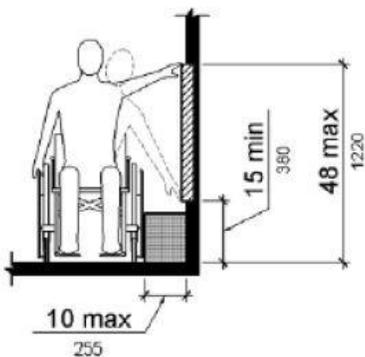
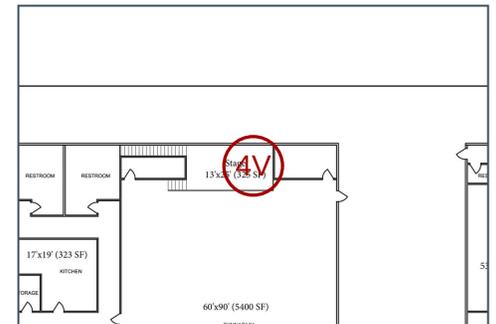


Figure 308.3.1 Unobstructed Side Reach

308.3.1  
 Kim Goss  
 Jun 28, 2021 11:10 AM
